



## STORMWATER MANAGEMENT PLAN NOTES:

- 1. THIS PLAN SHALL BE KEPT ON SITE AT ALL TIMES AND UPDATED TO REFLECT ANY CHANGES.
  - 2. CLEARING OR GRADING SHALL NOT BEGIN UNTIL ALL CONTROL MEASURES HAVE BEEN INSTALLED.
  - 3. CONTRACTOR IS RESPONSIBLE FOR INSTALLING AND MAINTAINING TEMPORARY EROSION AND SEDIMENT CONTROL MEASURES DURING CONSTRUCTION AND ESTABLISHING ANY REQUIRED PERMANENT CONTROL MEASURES TO PREVENT RELEASE OF POLLUTANTS FROM THE PROJECT SITE.
  - 4. CONTROL MEASURES SHALL BE USED, MODIFIED, AND MAINTAINED WHENEVER NECESSARY TO REFLECT CURRENT CONDITIONS. CONTROL MEASURES SHALL BE INSPECTED WEEKLY AND AFTER EVERY PRECIPITATION EVENT. ACCUMULATED SEDIMENT SHALL BE REMOVED FROM CONTROL MEASURES WHEN THE SEDIMENT LEVEL REACHES ½ THE HEIGHT OF THE CONTROL MEASURE.
  - 5. THE CONTRACTOR SHALL PROMPTLY REMOVE ALL SEDIMENT, MUD, AND CONSTRUCTION DEBRIS THAT MAY ACCUMULATE IN THE RIGHT OF WAY, PRIVATE PROPERTY, OR WATER WAYS AS A RESULT OF THE CONSTRUCTION ACTIVITIES.
  - 6. ALL INGRESS AND EGRESS ACCESS POINTS ON TO THE DISTURBED SITE MUST BE STABILIZED WITH A VEHICLE TRACKING CONTROL PAD. ACCESS SHALL ONLY BE VIA APPROVED LOCATIONS AS SHOWN ON APPROVED CSMP.
  - 7. TEMPORARY SOIL STABILIZATION MEASURES SHALL BE IMPLEMENTED WHERE GROUND DISTURBANCES HAVE TEMPORARILY OR PERMANENTLY CEASED FOR 14 DAYS OR FOR AREAS OF LAND DISTURBANCE WITHIN ONE GROWING SEASON.
  - CONCRETE WASTE AND WASHOUT WATER FROM MIXING TRUCKS SHALL BE CONTAINED ON SITE, REMOVED FROM THE SITE, AND PROPERLY DISPOSED.

    MATERIALS SHALL NOT BE ALLOWED TO ENTER STATE WATERS.
  - CONTRACTOR IS RESPONSIBLE FOR COMPLYING WITH ALL LOCAL, STATE, AND FEDERAL LAWS. IN ADDITION CONTRACTOR MUST OBTAIN REQUIRED PERMITS.
  - 10. EMERGENCY ACCESS MUST BE KEPT OBSTACLE FREE AND PASSABLE AT ALL TIMES.
  - 11. CONTRACTOR SHALL PROVIDE ADEQUATE WASTE MANAGEMENT INCLUDING BUT NOT LIMITED TO A REGULARLY MAINTAINED ON SITE DUMPSTER AND PORTA-POTTY.
  - 12. FINAL STABILIZATION IS THE CONDITION REACHED WHEN ALL GROUND SURFACE DISTURBING ACTIVITIES AT THE SITE HAVE BEEN COMPLETED, AND FOR ALL AREAS OF GROUND SURFACE DISTURBING ACTIVITIES A UNIFORM VEGETATIVE COVER HAS BEEN ESTABLISHED WITH AN INDIVIDUAL PLANT DENSITY OF AT LEAST 70 PERCENT OF PRE-DISTURBANCE LEVELS, OR EQUIVALENT PERMANENT, PHYSICAL EROSION REDUCTION METHODS HAVE BEEN EMPLOYED.

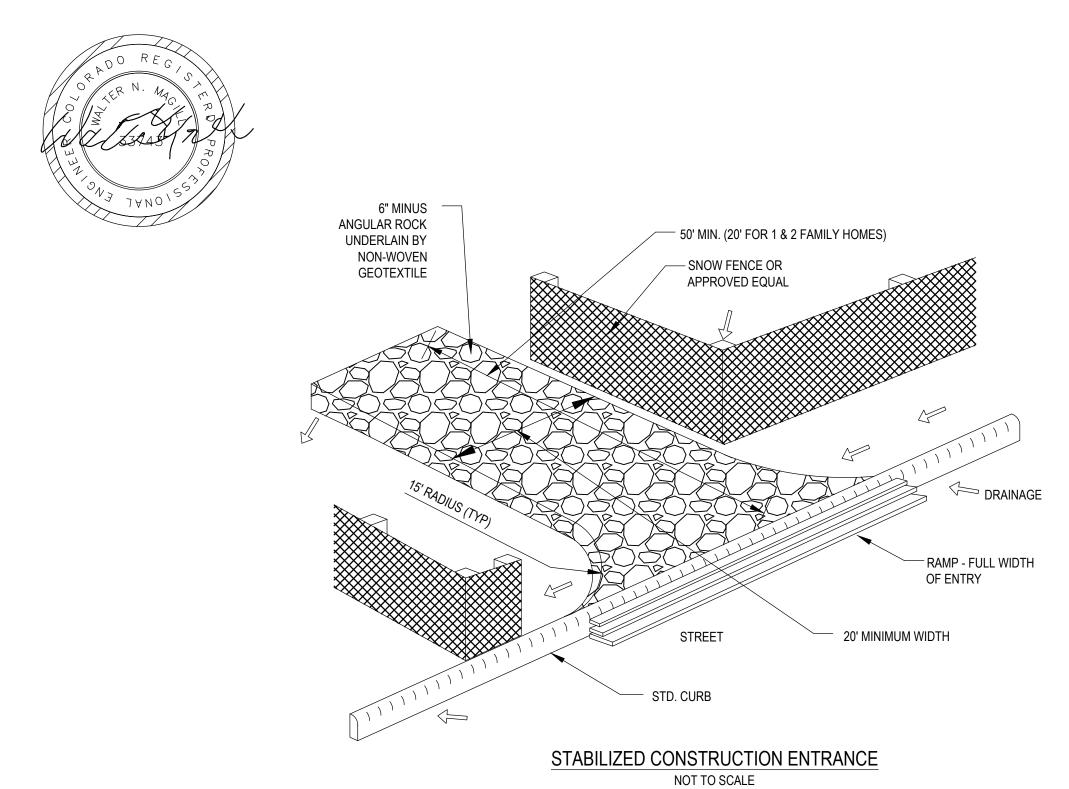

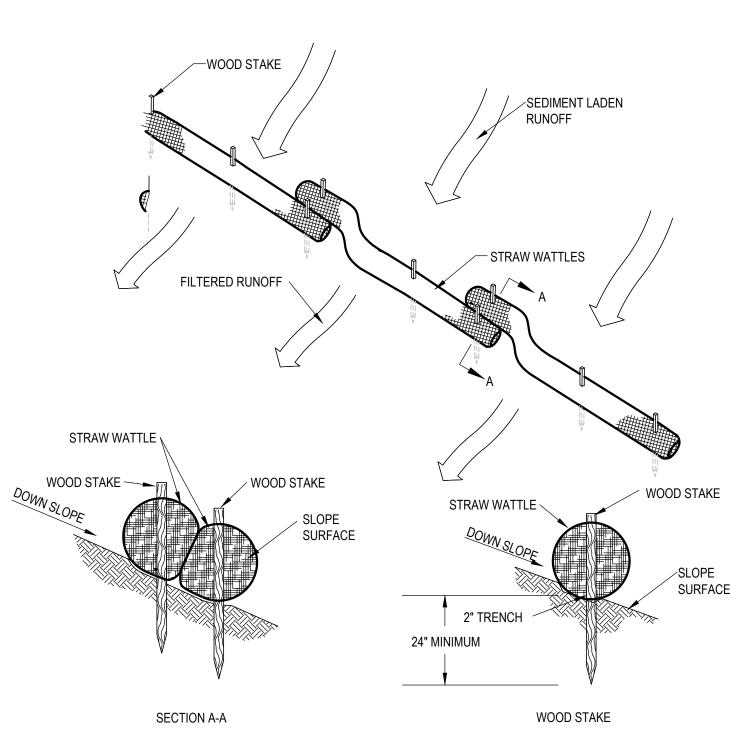

STRAW WATTLE DETAILS

NOT TO SCALE



440 S. Lincoln Ave, Suite 4A
P.O. Box 775966
Steamboat Springs, CO 80487
(970)-871-6772
www.fourpointsse.com

THUNDERSTICK ADVENTURE SUP AMENDMENT TBD HAYDEN, CO 81639

Horizontal Scale

0 20' 4

SCALE: 1" = 20'

Contour Interval = 2 ft

DATE: 6-13-2022

JOB #: 2118-002

DRAWN BY: DSC

DESIGN BY: CFB

REVIEW BY: WNM

IF THIS DRAWING IS PRESENTED IN A FORMAT OTHER THAN 24" X 36", THE GRAPHIC SCALE SHOULD BE UTILIZED.

FORMWATER ANAGEMENT PLAN

S

SHEET#

**C**2
